SAMPLE RESIDENCE

ITEM DESCRIPTION	DURATION	JULY					AUGUST																							
		T					M	T	W	TH	F	S	SU	M	T	W	TH	F	S	SU	M	T	W	TH	F	S	S	M	T	
PROJECT ITEMS		12					22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	
START DATE (PROJECTED)	**12-Jul**	1					6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	
RECEIVE PERMIT	1 DAY																													
SITE PREP	2 DAY																													
INTERIOR DEMO	5 DAYS																													
POOL DECK DEMO	3 DAY																													
CUT SLABS FOR PLUMBING RELOC.	2 DAY																													
PLUMB/ELECT UNDERGROUND	3 DAY																													
UNDERGROUND INSPECTION	1 DAY																													
DEMO ENTR/FILLED CELL/GARAGE	5 DAY																													
REBAR SLAB REPAIR	2 DAY																													
CUT/FILL	DAY																													
EXCAVATE FOOTERS	1 DAY																													
FORM FOOTERS	1 DAY																													
STEEL FOOTERS	1 DAY																													
MEP SLEEVES	1 DAY																													
PREP COMPACT SLAB ADD	2 DAY																													
TERMITE TREAT ADD	.5 DAY																													
VAPOR BARRIER ADD	.5 DAY																													
WELDED WIRE MESH ADD	.5 DAY																													
ORDER TRUSS PACKAGE	1 DAY																													
INSPECT SLAB	.5 DAY																													
POUR SLAB ADDITION	1 DAY																													
ORDER WINDOWS (7 WEEKS)	1 DAY																													
CMU BLOCK	1 DAY																													
REINFORCING INSPECTION	1 DAY																													
TIE BEAM FORM	1 DAY																													
TIE BEAM STEEL	1 DAY																													

TIE BEAM INSPECTION	1 DAY																											
ORDER PLUMBING FIXTURES	1 DAY																											
TIE BEAM/FILLED CELL POUR	1 DAY																											
PULL FORMS TIE BEAM	2 DAY																											
TRUSS INSTALLATION	3 DAY																											
TRUSS EXISTING TIE IN	1 DAY																											
TRUSS BLOCKING	1 DAY																											
TRUSS INSPECTION	1 DAY																											
PLYWOOD ROOF SHEATHING	3 DAY																											
PLYWOOD INSPECTION	1 DAY																											
HOT MOP	1 DAY																											
STACK ROOF	1 DAY																											
TILE ROOF INSTALLATION	3 DAY																											
ORDER INTERIOR DOORS 8WKS	1 DAY																											
ORDER HARDWARE	1 DAY																											
FUR WALLS/FRAME WALLS	2 DAY																											
ELECTRICAL ROUGHIN	7 DAY																											
PLUMBING ROUGHIN	4 DAY																											
MECHANICAL ROUGHIN	3 DAY																											
GAS ROUGH	2 DAY																											
ELECTRICAL ROUGH INSPECTION	1 DAY																											
PLUMB/GAS ROUGH INSPECTION	1 DAY																											
MECHANICAL ROUGH INSPECTION	1 DAY																											
WALL INSULATION	1 DAY																											
FRAMING INSPECTION	1 DAY																											
BACKING	2 DAY																											
DOOR AND WINDOW INSTALL	7 DAY																											
DOOR/WINDOW INSPECTION	1 DAY																											
ORDER APPLIANCES (90 DAYS)	1 DAY																											
STUCCO	5 DAY																											
GARAGE DOOR	2 DAY																											
DRYWALL CEILING	3 DAY																											
INTERIOR DOOR INSTALL	3 DAY																											
FINAL SURVEY	1 DAY																											

DRYWALL WALLS	3 DAY																											
SCREW INSPECTION	1 DAY																											
FINISH WALLS/CEILING	5 DAY																											
ORDER PLUMB/ELECT FIXTURES	1 DAY																											
PAINT INTERIOR	10 DAY																											
PAINT EXTERIOR	5 DAY																											
BATH TILE	12 DAY																											
INTERIOR FLOORING INSTALLATION	14 DAY																											
POOL DECK	5 DAY																											
BASEBOARD INSTALLATION	3 DAY																											
VANITY INSTALLATION	3 DAY																											
FINISH PAINTING	2 DAY																											
INSTALL KITCHEN CABINETS	5 DAY																											
TEMPLATE GRANITE	.5 DAY																											
INSTALL GRANITE COUNTERTOPS	2 DAY																											
APPLIANCE DELIVERY	.5 DAY																											
PLUMBING TRIM	5 DAY																											
ELECTRICAL TRIM	5 DAY																											
MECHANICAL TRIM	3 DAY																											
GAS TRIM	1 DAY																											
FINAL MEP INSPECTIONS	1 DAY																											
DRIVEWAY	4 DAY																											
FINAL BUILDING INSPECTION	1 DAY																											
FINAL CLEANING	5 DAY																											
PUNCHLIST ITEMS	14 DAY																											

OCTOBER

W	TH	F	S	S	M	T	W	TH	F	S	SU	M	T	W	TH	F	S	SU	M	T	W	TH	F	S	SU	M	T	W	TH	F	S	SU	M	T	W	TH	F	S	SU	M	T	W	TH
14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27
29	30	31	32	33	34	35	36	37	38	39	40	41	42	43	44	45	46	47	48	49	50	51	52	53	54	55	56	57	58	59	60	61	62	63	64	65	66	67	68	69	70	71	72

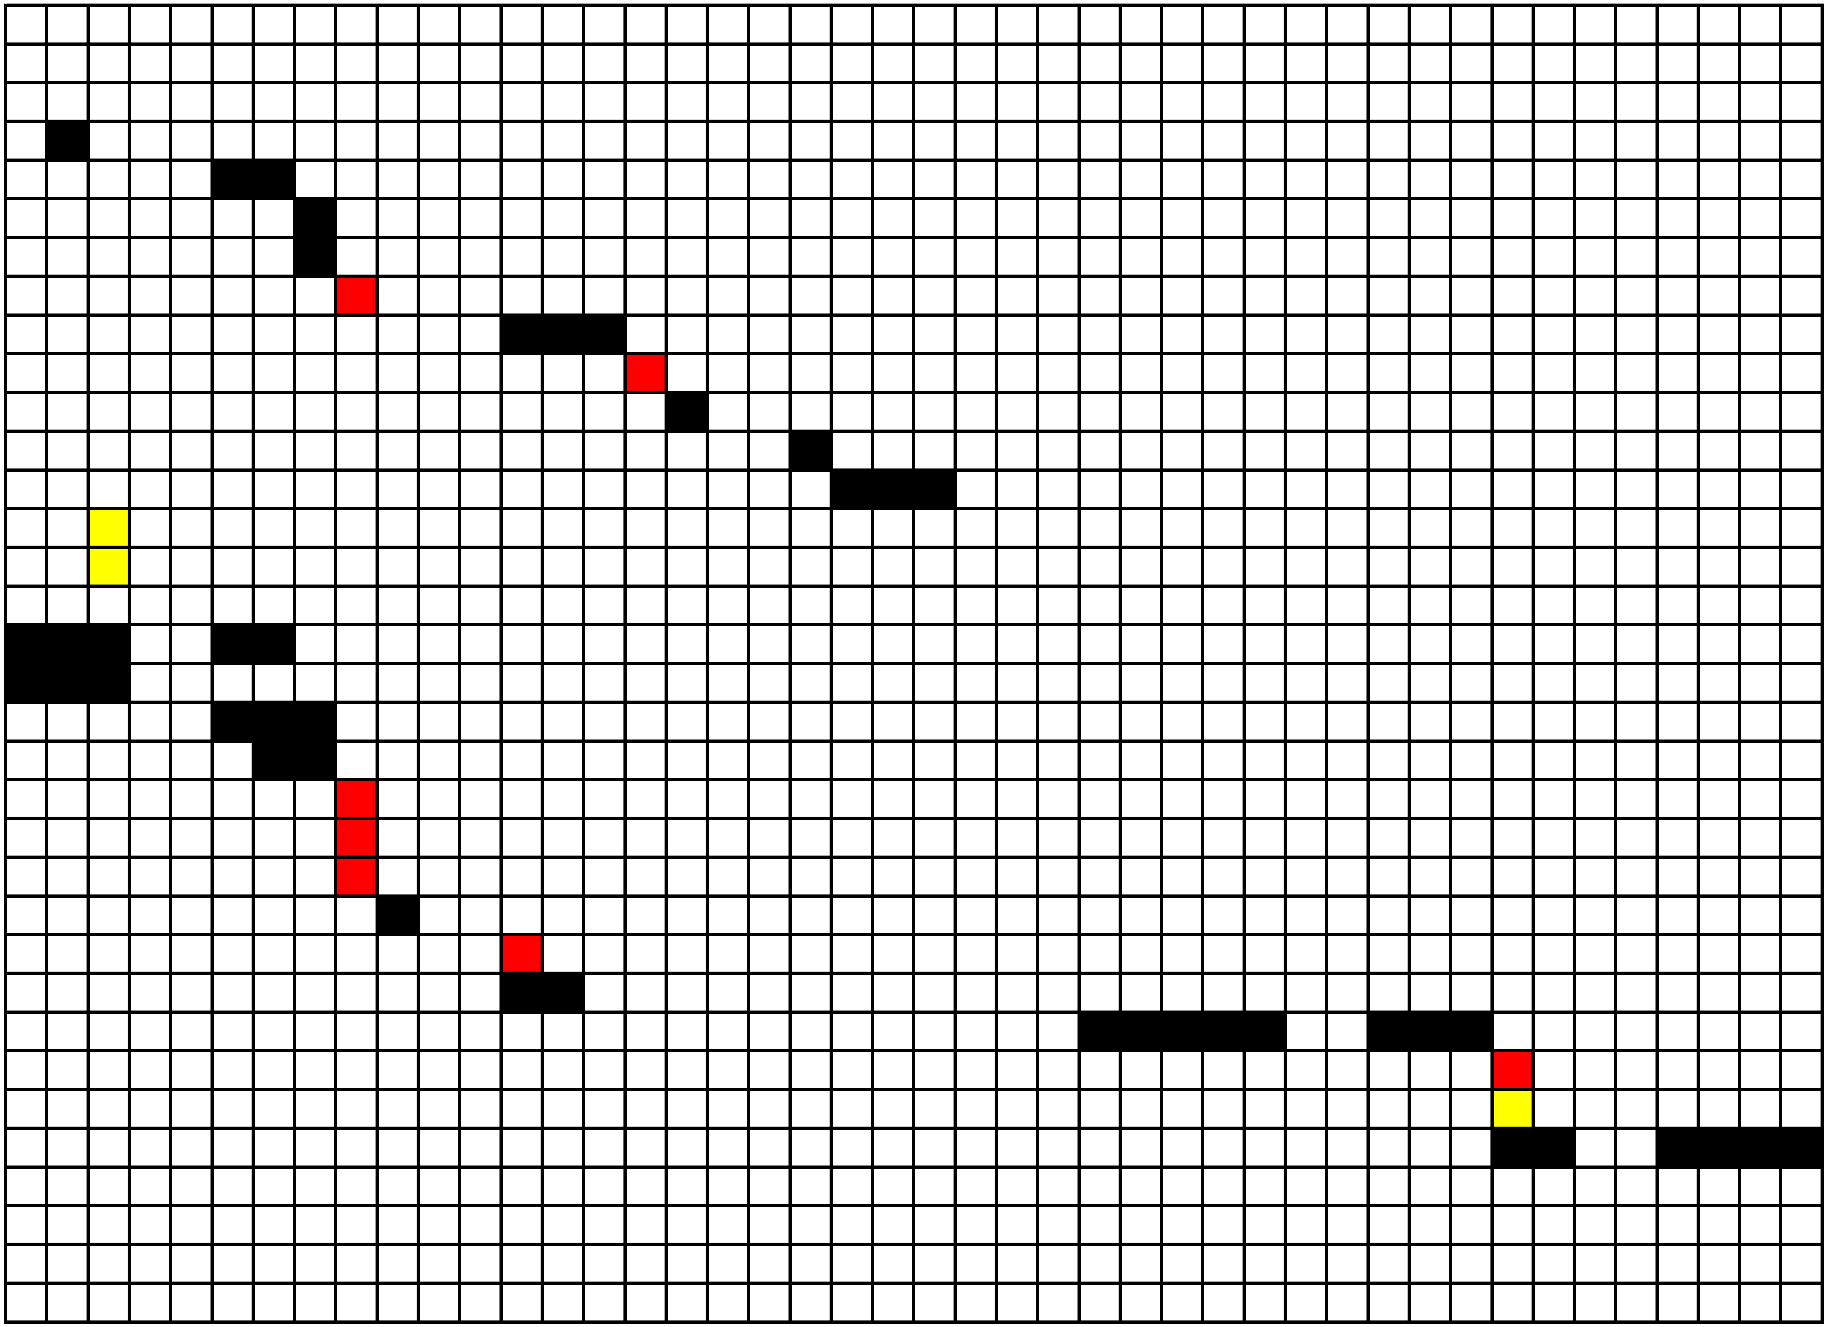

NOVEMBER **DECEMBER**

F	S	SU	M	T	W	TH	F	S	SU	M	T	W	TH	F	S	SU	M	T	W	TH	F	S	SU	M	T	W	TH	F	S	SU	M	T	W	TH	F	S	SU	M	T	W	TH	F	S
28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	1	2	3	4	5	6	7	8	9	10
73	74	75	76	77	78	79	80	81	82	83	84	85	86	87	88	89	90	91	92	93	94	95	96	97	98	99	100	101	102	103	104	105	106	107	108	109	110	111	112	113	114	115	116

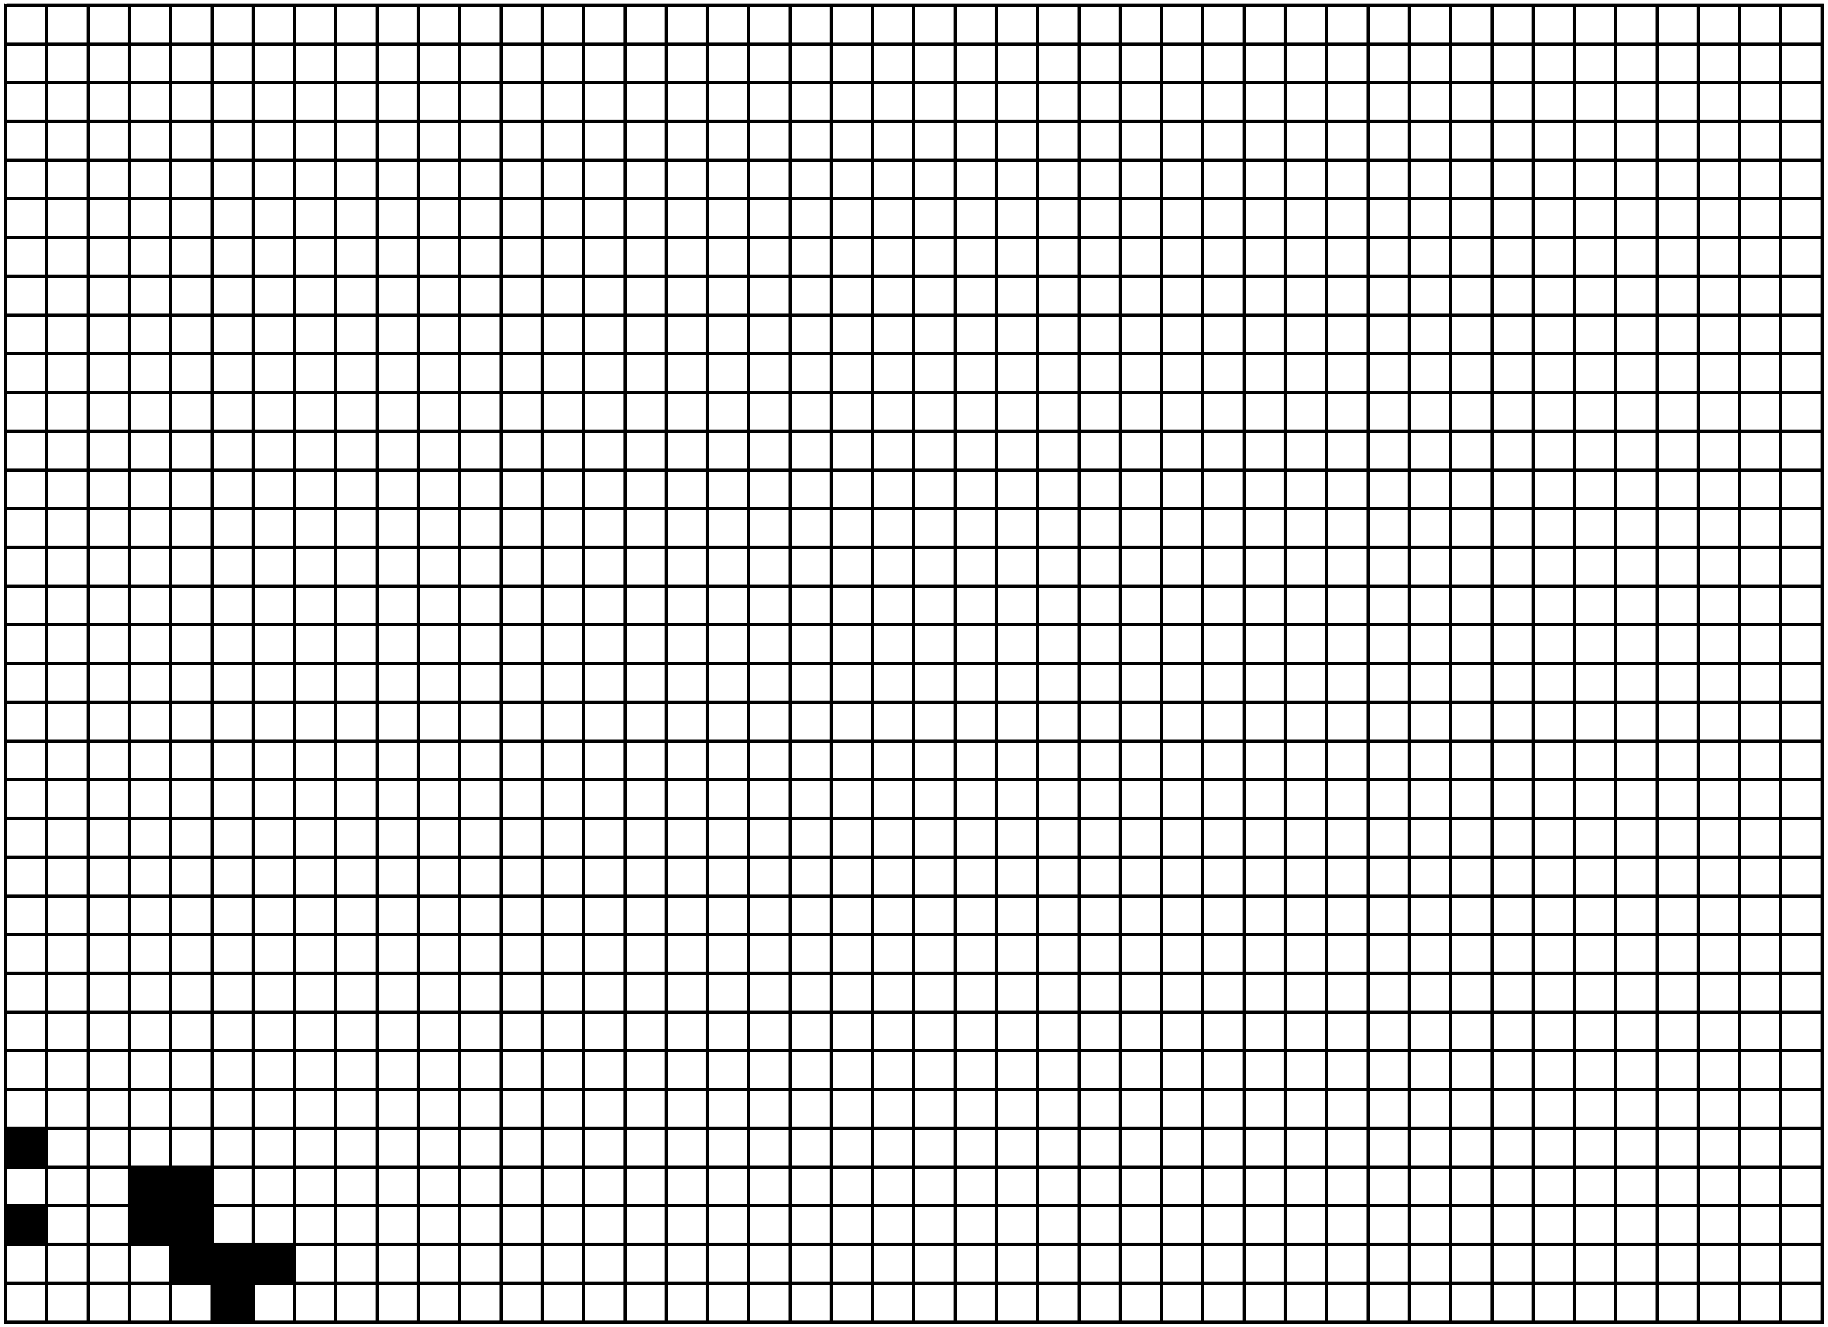

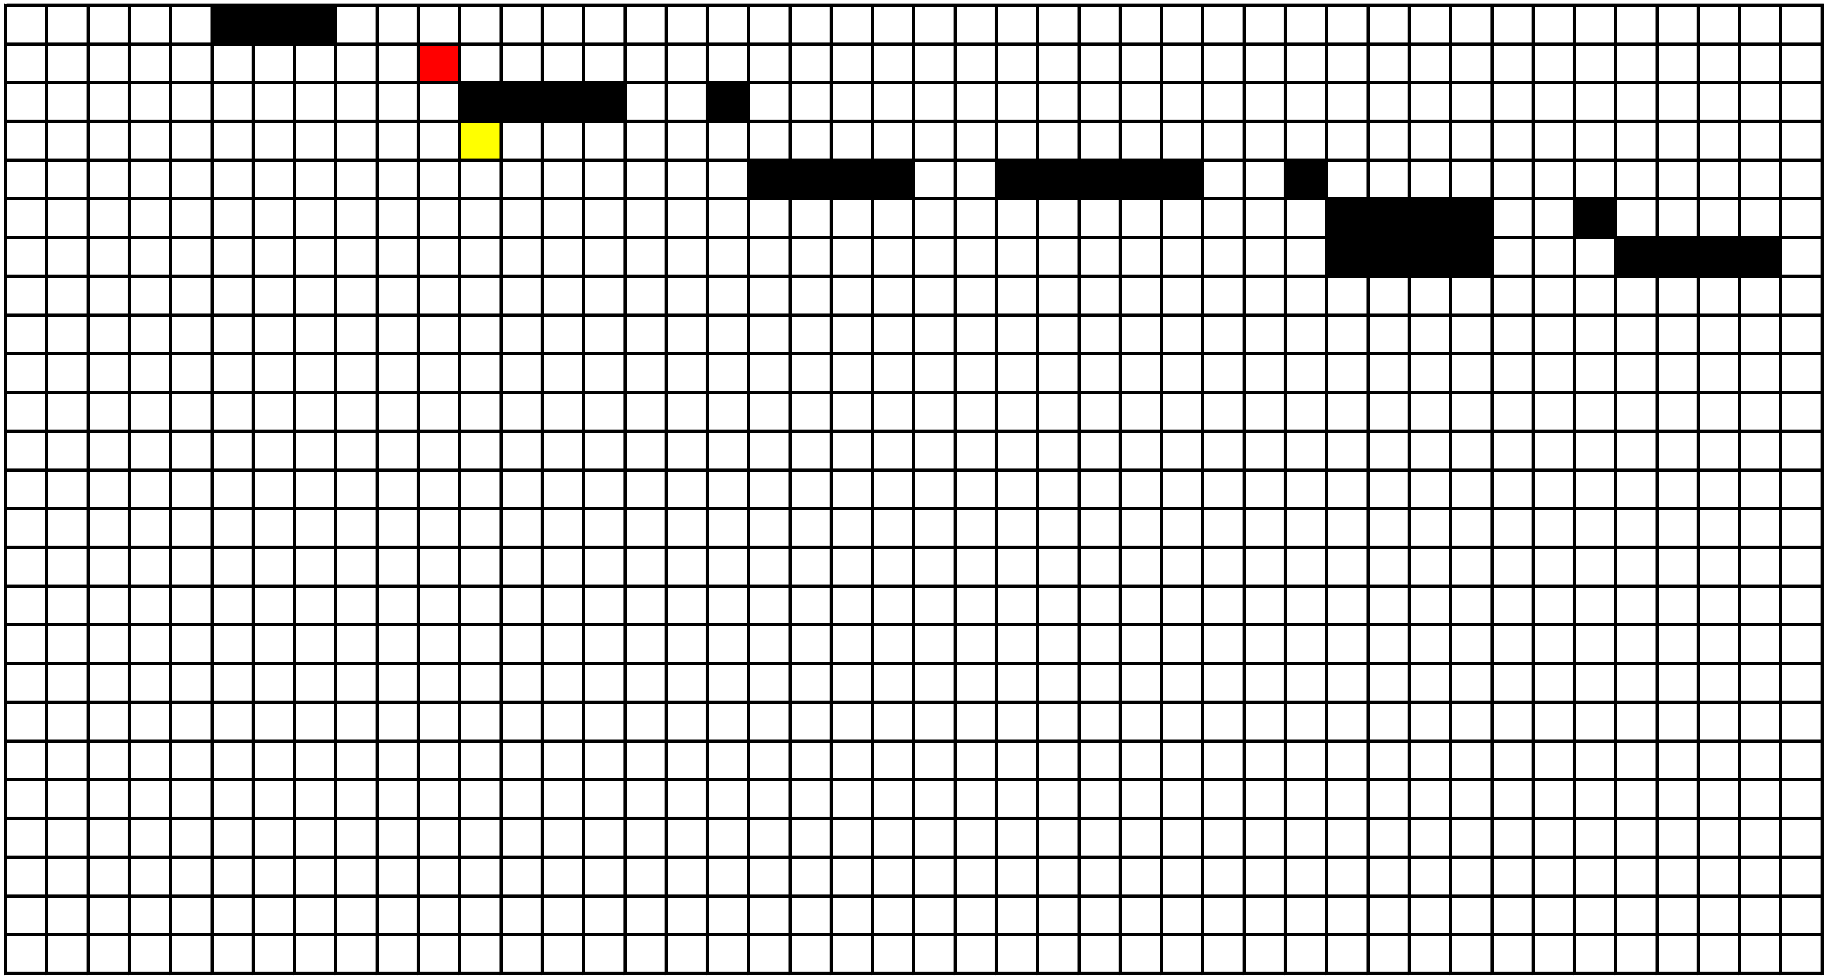

JANUARY

SU	M	T	W	TH	F	S	SU	M	T	W	TH	F	S	SU	M	T	W	TH	F	S	SU	M	T	W	TH	F	S	SU	M	T	W	TH	F	S	SU	M	T	W	TH	F	S	SU	M
11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23
117	118	119	120	121	122	123	124	125	126	127	128	129	130	131	132	133	134	135	136	137	138	139	140	141	142	143	144	145	146	147	148	149	150	151	152	153	154	155	156	157	158	159	160

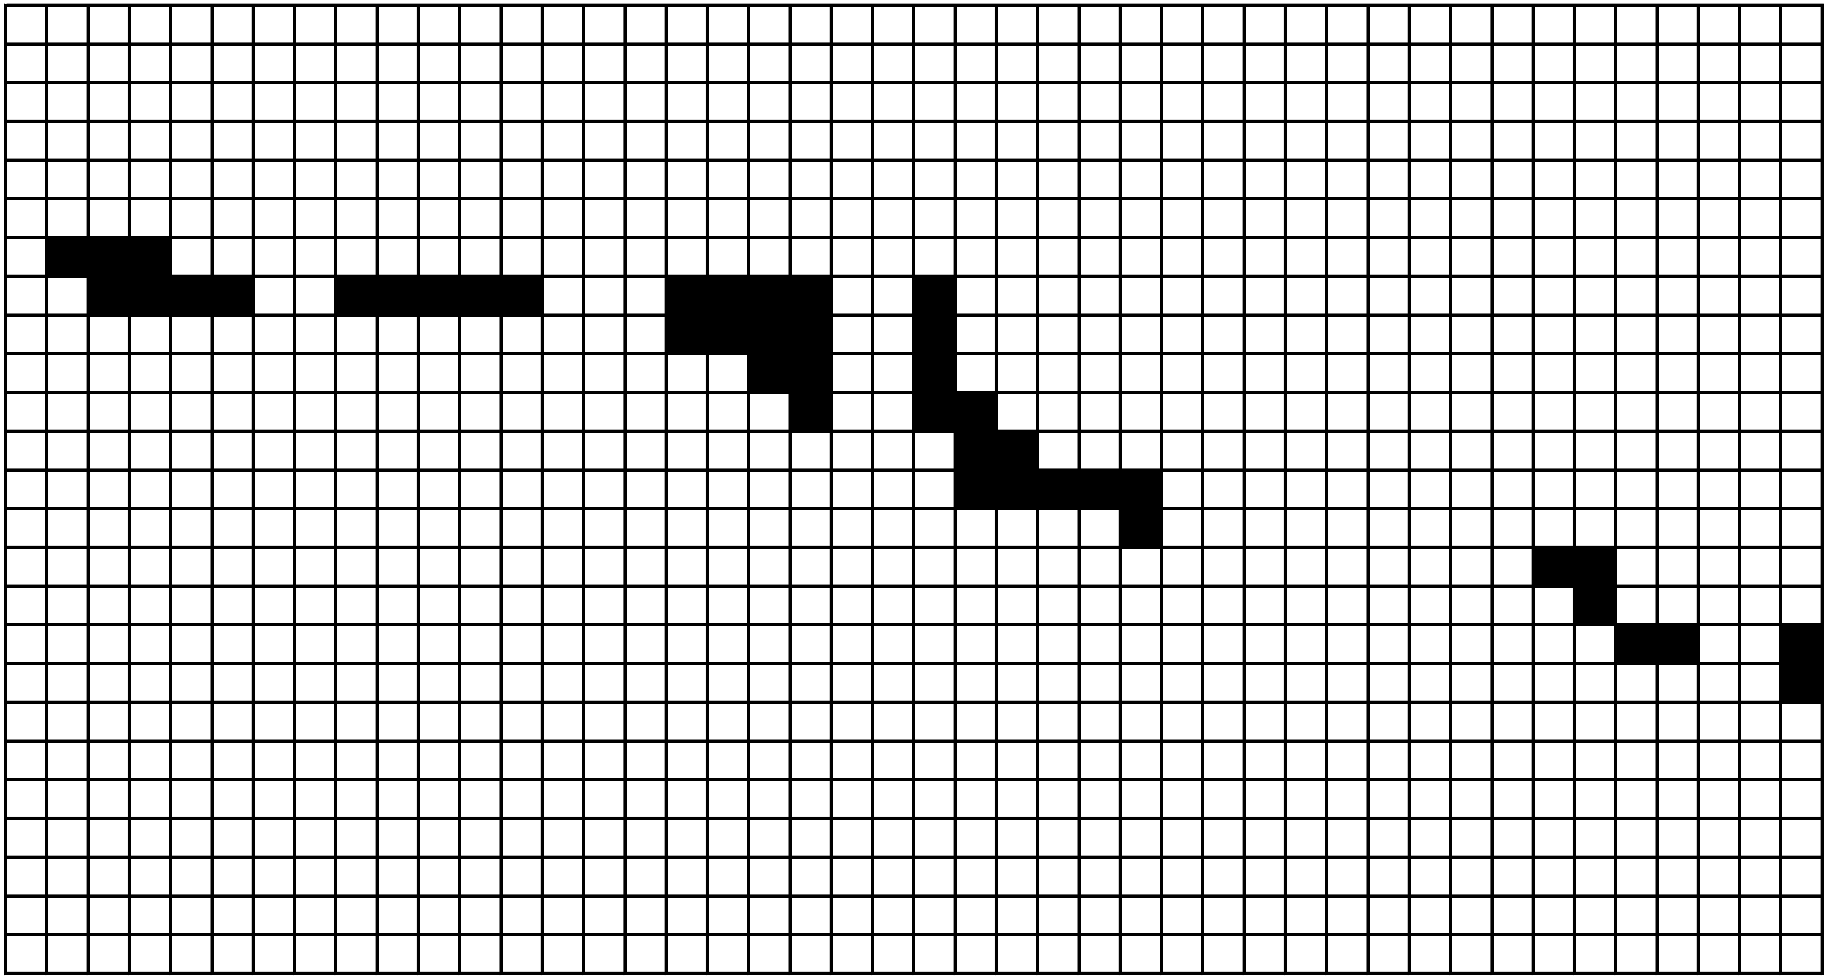

FEBRUARY
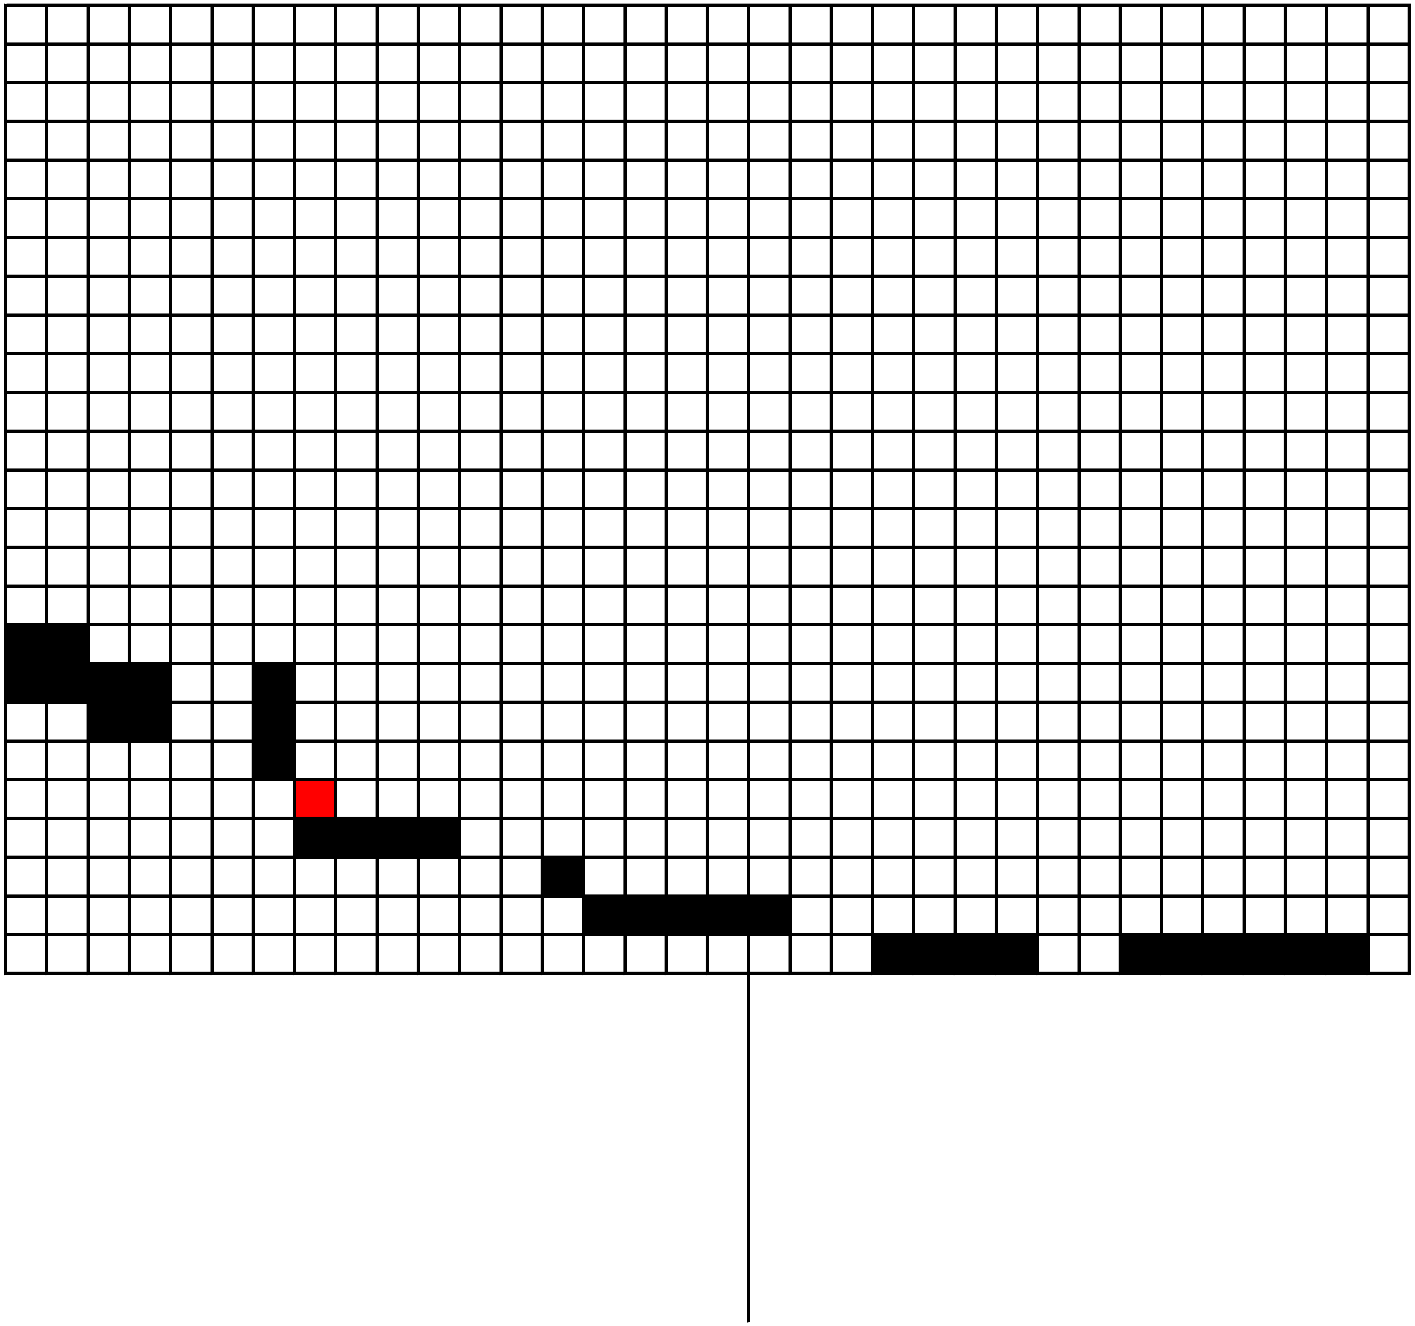
T	W	TH	F	S	SU	M	T	W	TH	F	S	SU	M	T	W	TH	F	S	SU	M	T	W	TH	F	S	SU	M	T	W	TH	F	S	SU
24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26
161	162	163	164	165	166	167	168	169	170	171	172	173	174	175	176	177	178	179	180	181	182	183	184	185	186	187	188	189	190	191	192	193	194
